ACME CORP — PROJECT STATUS

Acme HQ Office Renovation


Status as of 19 April 2026

OVERALL COMPLETE	MILESTONES	SCHEDULE HEALTH	TARGET HANDOVER
28%	2 / 9	At risk	25 Sep
Across 14 tasks	Achieved	1 at risk • 0 slipped	2026

> *Design phase substantially complete. Permits are the current critical path with a five-day slip — mobilisation for construction is still tracking to 4 May.*

Schedule

14 TASKS · 4 PHASES

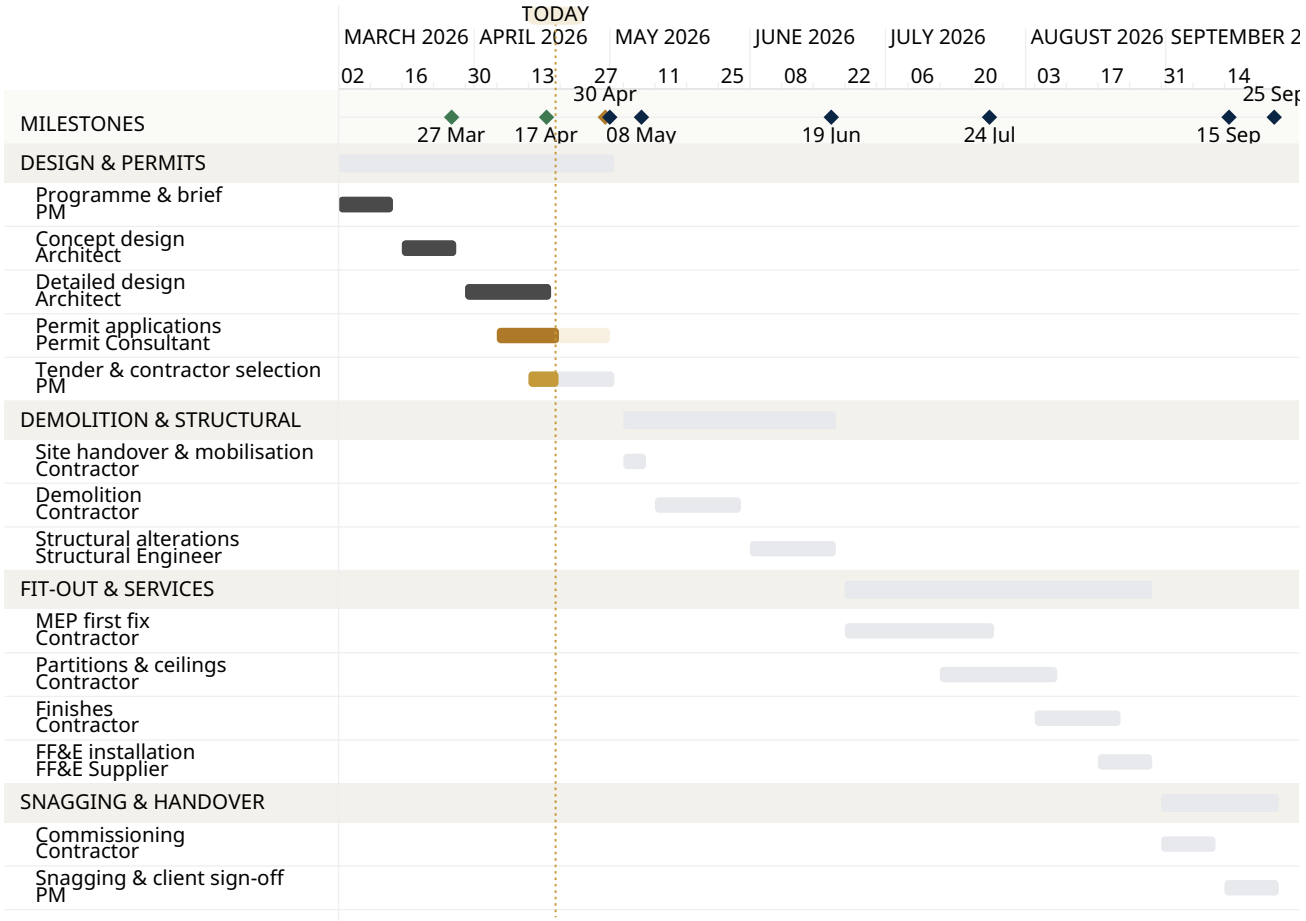

Milestones

2 ACHIEVED · 7 AHEAD

27 MAR — Concept design approved

17 APR — Detailed design sign-off

30 APR — Permits approved

01 MAY — Contractor appointed

08 MAY — Site handover

19 JUN — Structural alterations complete

24 JUL — MEP first fix complete

15 SEP — Practical completion

25 SEP — Handover to client

Concept design approved

27 MAR 2026

Client signed off the concept design and footprint.

Achieved · Architect

Detailed design sign-off

17 APR 2026

Detailed drawings, spec, and FF&E schedule approved.

Achieved · Architect

Permits approved

30 APR 2026

City sign-off on building and mechanical permits. Currently five working days behind the target date.

At risk · Permit Consultant

Contractor appointed

01 MAY 2026

Signed main contract with preferred contractor.

On track · PM

Site handover

08 MAY 2026

Physical handover of the building to the main contractor for works.

On track Contractor

Structural alterations complete

19 JUN 2026

All demolition and structural changes signed off by the engineer.

On track Structural Engineer

MEP first fix complete

24 JUL 2026

Mechanical, electrical, and plumbing first fix signed off.

On track Contractor

Practical completion

15 SEP 2026

Building is safe to occupy; snag list issued.

On track PM

Handover to client

25 SEP 2026

All snags cleared, documentation and warranties transferred.

On track PM

Review needed before sending

MILESTONES · M03 Permit sign-off is trending five working days behind the internal target. Recommend the client clears a pre-meeting slot with the city permits office in the next ten days to de-risk the 30 April date.
